

Construction in Photos

May 2 - 13, 2016

Water Resource Recovery Department Village of Ashville Ashville's Water Resource Recovery Facility Part A

Presentation Available on Line at:

www.ashvilleohio.gov



Ashville's WRRF Project



Construction in Photos



- May 2, 2016
- Digester excavation prior to dewatering and continued excavation.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos

- May 2, 2016
- The UV/Post Air tank base slab excavation prior to dewatering.
- Job No: 60440011



Ashville's WRRF Project



Construction in Photos




- May 2, 2016
- The UV/Post Air Influent Section base slab excavation prior to dewatering and form removal.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos

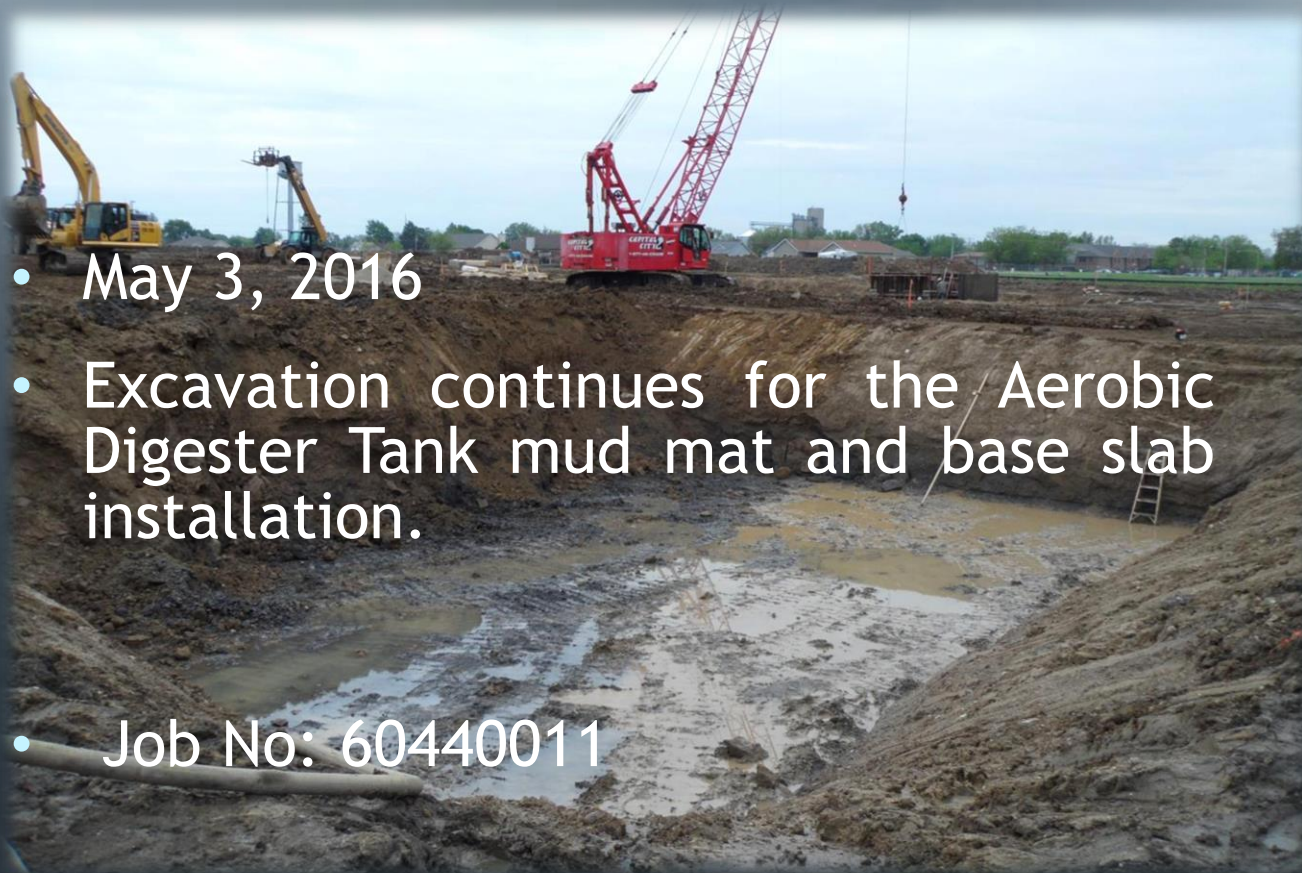

- May 3, 2016
- Excavation continues for the Aerobic Digester Tank mud mat and base slab installation.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos



- May 3, 2016
- The inner Southwest corner of UV/Post Air tank wall forms.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos



- May 3, 2016
- The UV/Post Air tank South inner wall forms measuring 24 ft. long and 16 ft. high.

Job No: 60440011

Ashville's WRRF Project



Construction in Photos



- May 3, 2016
- The first North inner wall form measuring 12 ft. wide by 16 ft. high of the UV/Post Air tank has been set in place.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos

- May 4, 2016
- Cleaning up around the UV/Post Air Tank influent section mud mat and base slab.
- Job No: 60440011



Ashville's WRRF Project



Construction in Photos



- May 4, 2016
- Excavation continues for the Aerobic Digester Tank mud mat and base slab installation.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos



- May 5, 2016
- Progress on the UV/Post Air tank wall rebar installation.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos

- May 5, 2016
- The #57 gravel, dewatering sump and cleaned UV/Post Air tank influent section base slab. Ready for wall form installation.

• Job No: 60440011



Ashville's WRRF Project



Construction in Photos




- May 5, 2016
- The 24-inch effluent discharge pipe wall sleeve installed on the UV/Post Air Tank.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos

- May 5, 2016
- UV/Post Air/Tank influent section base slab inner wall forms.

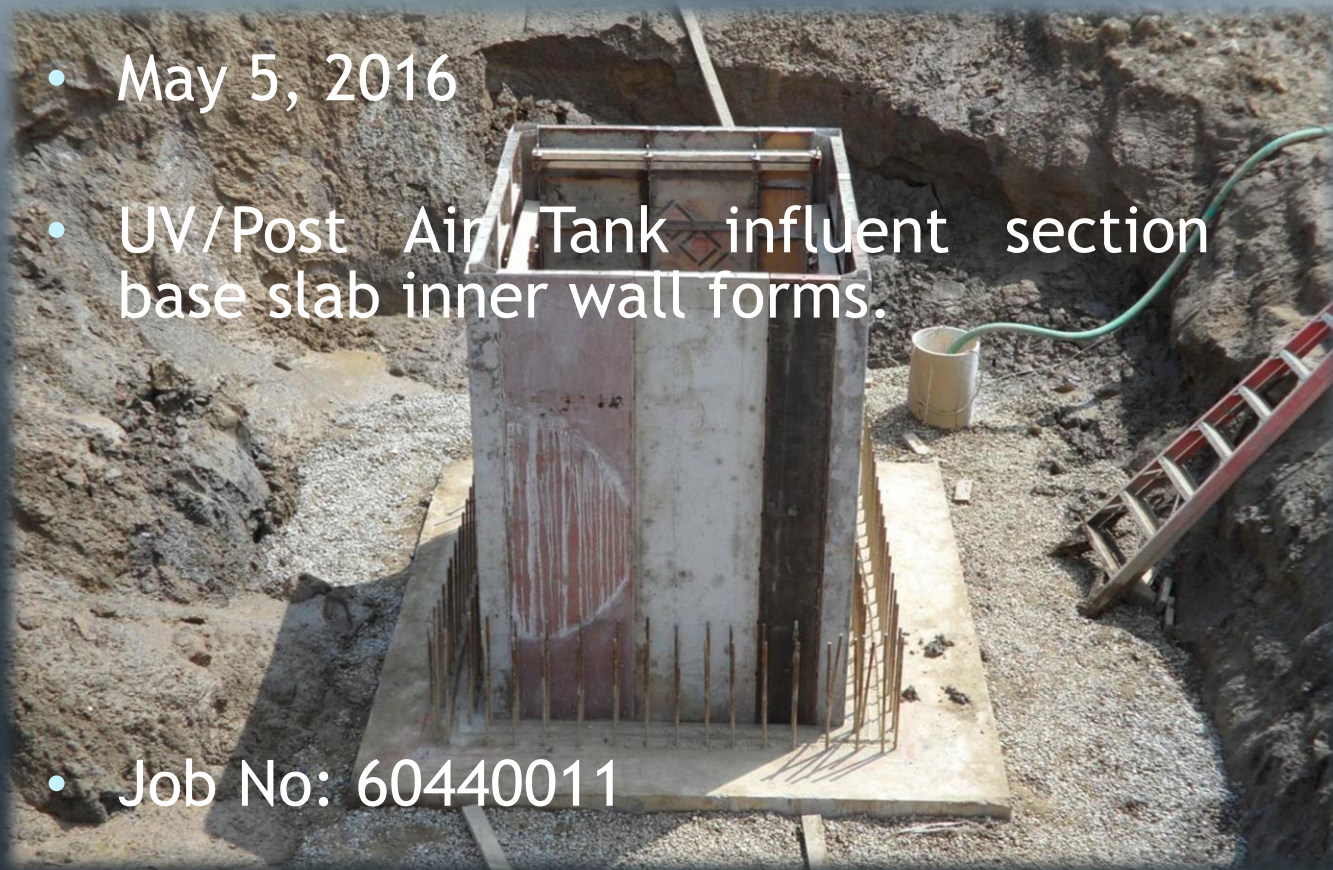

- Job No: 60440011

Ashville's WRRF Project



Construction in Photos



- May 5, 2016
- Excavation continues for the Aerobic Digester Tank mud mat and base slab installation.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos

- May 6, 2016
- Progress continues on the UV/Post Air tank wall rebar installation.



Job No: 60440011

Ashville's WRRF Project



Construction in Photos



- May 6, 2016
- Temporary Electric Service rack to assist in construction activities at the UV/Post Air and Aerobic Digester Tank excavation sites.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos



- May 6, 2016
- Installation begins on the wall rebar for the Influent section of the UV/Post Air tank.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos



- May 6, 2016
- Excavation continues for the Aerobic Digester mud mat and base slab installation.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos



- May 6, 2016
- Progress continues on the UV/Post Air tank wall rebar and form installation.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos



- May 10, 2016
- The Post Air tank partial wall forms are complete and ready for the first concrete pour.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos



- May 10, 2016
- The influent section (UV/Post Air) inner wall forms in place and the rebar installation partially completed.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos



- May 11, 2016
- The UV/Post Air influent section wall form and rebar installation partially complete.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos



- May 13, 2016
- The Post Air Tank wall form installation continues.
- Job No: 60440011

Ashville's WRRF Project



Construction in Photos



- May 13, 2016
- Ashville WRRF Improvements 2015 - part A.
- Job No: 60440011



Next Step Part B

THANK YOU

ASHVILLE 
Vision Statement
