

Construction in Photos

June 1 - 30, 2017

Water Resource Recovery Department Village of Ashville Ashville's Water Resource Recovery Facility Part B-Job No: 60440011

Presentation Available on Line at:

www.ashvilleohio.gov



Ashville's WRRF Project



Construction Aerial Photo



For up-to-date information go to www.ashvilleohio.gov and click on the following image:



or call 740-983-6367



Effluent Line

Time-line below:

- January 2-13 mobilization & materials
- January 16 or 18 construction begins at Scioto & Rich Street (MH 8)
- January 29 Rich Street & Rodger Alley (MH 9A)
- January 23 or 26 Lexington Avenue & May Street (just south of MH 18 at MH 20)
- February 14 Rodger Alley & Madison Avenue (MH 10)
- February 22 Rodger Alley & Griggs Street (MH 11)
- March 1 Rodger Alley & West Station Street (MH 12)

Force Main

Time-line below:

- February 21 Rich Street & Scioto Street
- March 5 Rich Street & Lexington Avenue
- March 12 Lexington Avenue & Madison Avenue
- March 19 Lexington Avenue & Griggs Street
- March 26 Lexington Avenue & West Station Street



Ashville's WRRF Project



Construction in Photos



- June 1, 2017
- Crew installed 6" of #2 limestone and geotextile fabric for the embankment area of the Haddox Property.

Ashville's WRRF Project



Construction in Photos



- June 1, 2017
- Crew installed 6" of #2 limestone and geotextile fabric on the embankment area of the Haddox Property.

Ashville's WRRF Project



Construction in Photos



- June 1, 2017
- Concrete Crew excavated and installed the 2 x 4 concrete forms and 2" of #304 granular for the 4" concrete sidewalk on Scioto St. from the Alley to Rich St.

Ashville's WRRF Project



Construction in Photos



- June 1, 2017
- Concrete Crew pouring 7 yards of ODOT Class "C" concrete for the 4" concrete sidewalk and curb on Scioto St. from the Alley to Rich St.

Ashville's WRRF Project



Construction in Photos



- June 2, 2017
- Crew performing restoration work on the 10" Force Main trench line on Scioto St. from the Alley to Rich St.

Ashville's WRRF Project



Construction in Photos



- June 2, 2017
- Concrete Crew installing the 2 x 4 concrete forms and #304 granular for the 4" concrete sidewalk on Scioto St. from the alley to Rich St.

Ashville's WRRF Project



Construction in Photos



- June 2, 2017
- Concrete Crew pouring 5 yards of ODOT Class "C" concrete for the 4" concrete sidewalk on Scioto St. from the Alley to Rich St.

Ashville's WRRF Project



Construction in Photos



- June 2, 2017
- Crew performed restoration, seeding and mulching on the 10" Force Main trench line and the least section of 18" Sewer from MH#19 to MH# 20 in the laydown area.

Ashville's WRRF Project



Construction in Photos



- June 5, 2017
- Crew installing the concrete forms for the curb and driveway on Scioto St. from Main St. to the First Alley.

Ashville's WRRF Project



Construction in Photos



- June 5, 2017
- Crew has completed the concrete forms for the curb and driveway on Scioto St.

Ashville's WRRF Project



Construction in Photos



- June 5, 2017
- Crew pouring 7 yards of ODOT Class "C" concrete for the 7" curb and driveway on Scioto St. from Main St. to the first alley.

Ashville's WRRF Project



Construction in Photos



- June 5, 2017
- Crew installing grout for the pipe inverts of the 24" Outfall Sewer.

Ashville's WRRF Project



Construction in Photos



- June 6, 2017
- Crew starting to excavate to install the 8 inches of ODOT #301 Asphalt Base at the intersection of Main St. and Scioto St.

Ashville's WRRF Project



Construction in Photos



- June 6, 2017
- Crew installing item #407 tack coat to the edges of the existing asphalt before the #301 asphalt base is installed.

Ashville's WRRF Project



Construction in Photos




- June 6, 2017
- Crew installing the first section of #301 Asphalt Base at the intersection of Main St. and Scioto St.

Ashville's WRRF Project



Construction in Photos

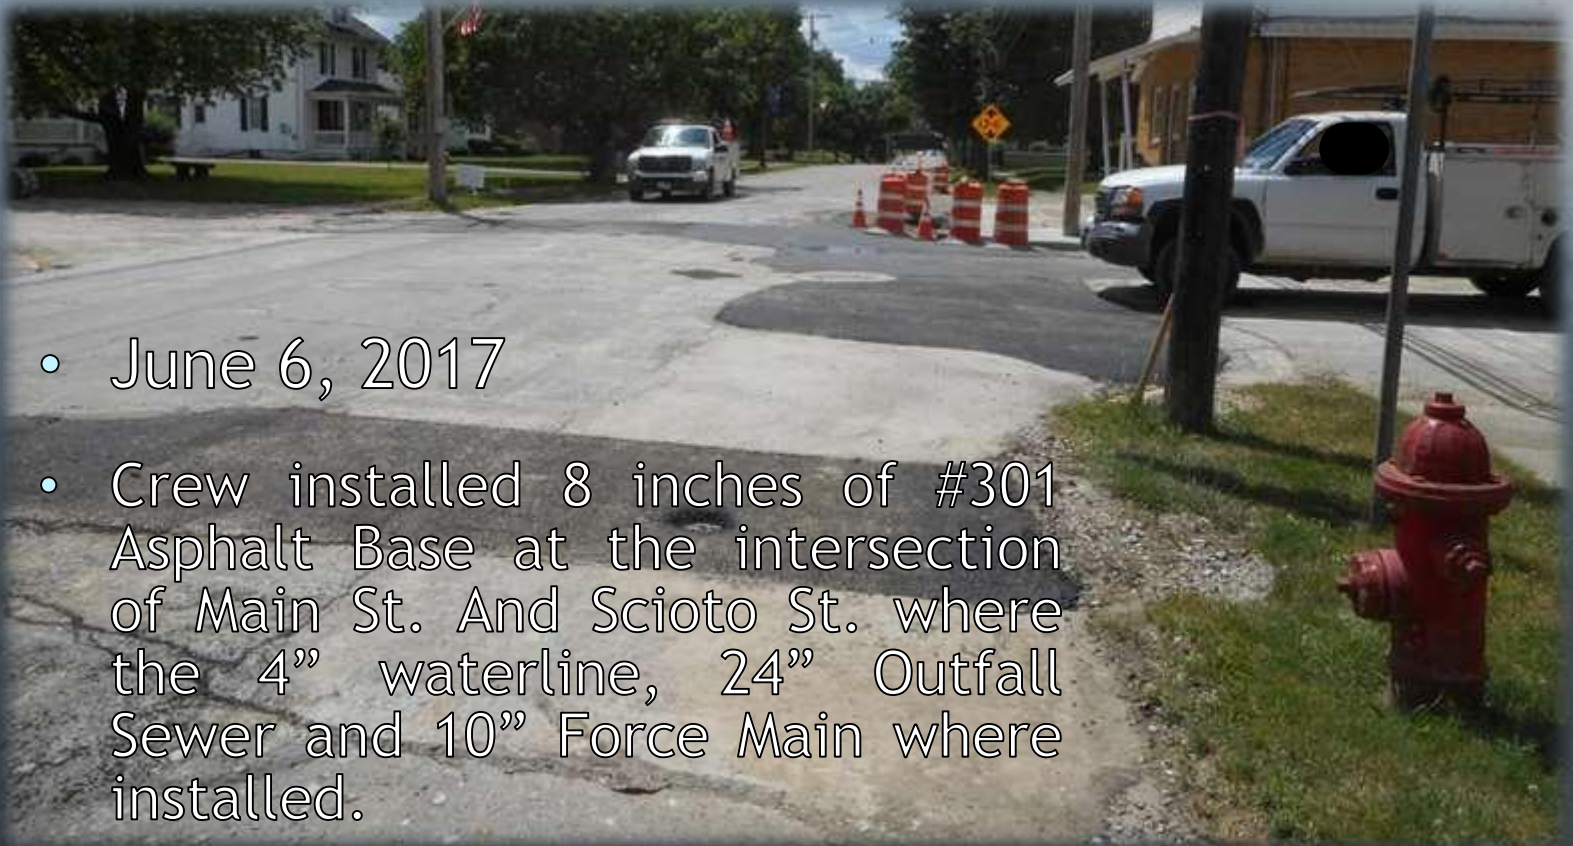

- June 6, 2017
- Crew installed 8 inches of #301 Asphalt Base at the intersection of Main St. And Scioto St. where the 4" waterline, 24" Outfall Sewer and 10" Force Main were installed.

Ashville's WRRF Project



Construction in Photos



- June 7, 2017
- Crew installing the last section of 8" #301 Asphalt Base at the intersection of Main St. And Scioto St.

Ashville's WRRF Project



Construction in Photos



- June 7, 2017
- Crew installing the ODOT Class "C" concrete for the driveway at #49 Scioto St.

Ashville's WRRF Project



Construction in Photos



- June 7, 2017
- Crew finishing the concrete sidewalk, curb and gutter on the corner of Scioto St. and Rich St.

Ashville's WRRF Project



Construction in Photos



- June 8, 2017
- Crew poured 4 yards of ODOT Class "C" concrete for the new driveway at the old WWTP.

Ashville's WRRF Project



Construction in Photos



- June 8, 2017
- Crew installed the concrete forms for the sidewalk and curb/gutter at the intersection of Jefferson St. and Rich St.

Ashville's WRRF Project



Construction in Photos



- June 8, 2017
- Crew poured 4 yards of ODOT Class "C" concrete for the sidewalk and curb/gutter at the intersection of Jefferson St. and Rich St.

Ashville's WRRF Project



Construction in Photos



- June 12, 2017
- Crew installing the concrete forms for one of the three curb and gutter repairs on Lexington Ave.

Ashville's WRRF Project



Construction in Photos



- June 12, 2017
- Crew poured 4 yards of ODOT Class "C" concrete for the three curb and gutter repairs on Lexington Ave.

Ashville's WRRF Project



Construction in Photos



- June 12, 2017
- Crew seeding and Mulching the sidewalk and curb/gutter at the intersection of Jefferson Ave. and Rich St.

Ashville's WRRF Project



Construction in Photos



- June 13, 2017
- Crew installing #304 limestone around the new driveway at the Old WWTP.

Ashville's WRRF Project



Construction in Photos



- June 13, 2017
- Crew installed topsoil, seed, fertilizer and straw mulch on the three curb/gutter repairs on Lexington Ave. The three photos above show the North, Middle and South locations along the 10" Force Main trench line.

Ashville's WRRF Project



Construction in Photos



- June 26, 2017
- Crew excavating the 6" sanitary service lateral at 49 Scioto St. the had a low section in the line.

Ashville's WRRF Project



Construction in Photos



- June 26, 2017
- Crew has removed the old 6" SDR-35 PVC sewer pipe and installed this new 6" SDR-35 PVC sewer pipe at 49 Scioto St.

Ashville's WRRF Project



Construction in Photos



- June 27, 2017
- Crew installing cleaning out and resetting the casting on existing MH#66 in the laydown area.

Ashville's WRRF Project



Construction in Photos



- June 27, 2017
- Fields located and raised the two curb boxes on the Haddox property.



Ashville's WRRF Project



Construction in Photos



- June 28, 2017
- Crew working on raising the casting on new storm MH#26 at Roger Alley and Madison Ave.

Ashville's WRRF Project



Construction in Photos



- June 28, 2017
- New storm MH#26 has been raised to proper grade at Roger Alley and Madison Ave.



**THANK YOU
AECOM, FIELDS, AND PETERSON**

ASHVILLE
Vision Statement
