Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
GENERAL REQUIREMENTS					
1000	NOTICE TO PROCEED	1	0	10MAR16A	10MAR16A
4000	MOBILIZE	10	0	21MAR16A	25MAR16A
1020	NEW PLANT COMMISSIONING	38	38	13JUL17	04SEP17
4030	CONTRACT B COMPLETED	1	1	31JUL17*	31JUL17
1030	PUT NEW PLANT ON-LINE	1	1	07SEP17	07SEP17
1040	PLANNED SUBSTANTIAL COMPLETION	1	1	08SEP17	08SEP17
1060	CONTRACT SUBSTANTIAL COMPLETION	1	1	11SEP17*	11SEP17
1010	PUNCH LIST	20	20	11SEP17	06OCT17
1050	PLANNED FINAL COMPLETION	1	1	20OCT17	20OCT17
1070	CONTRACT FINAL COMPLETION	1	1	09NOV17	09NOV17
SITEWORK - NEW PLANT					
1080	ACCESS ROAD	7	0	21MAR16A	30MAR16A
1240	CLEAR TREES	10	0	22MAR16A	30MAR16A
1150	TEMPORARY FENCING	5	0	11APR16A	15APR16A
1090	STRIP TOPSOIL	15	2	14APR16A	10MAR17
1140	NORTH PERMANENT FENCE	5	0	18APR16A	29APR16A
1220	WATER MAIN	4	0	19MAY16A	24MAY16A
1230	YARD PROCESS PIPING	200	60	01JUN16A	31MAY17
1190	UNDERGROUND ELECTRIC	150	15	05OCT16A	29MAR17
1200	GENERATOR PAD	5	0	28NOV16A	30NOV16A
1210	SET GENERATOR	2	0	20DEC16A	21DEC16A
1180	SITE GAS	5	5	02JUN17	08JUN17
1100	SITE CUTS/FILLS	20	20	22JUN17	19JUL17
1110	SITE CONCRETE	10	10	20JUL17	02AUG17
1170	STONE DRIVES	10	10	20JUL17	02AUG17
1160	BALANCE OF PERMANENT FENCE	5	5	20JUL17	26JUL17
1120	ASPHALT	5	5	03AUG17	09AUG17
1130	SEEDING	5	5	13OCT17	19OCT17
INFLUENT PUMP STATION - NEW PLANT					
1250	EXCAVATE/SET WETWELL/BACKFILL	10	0	13OCT16A	26OCT16A
4040	ADDITIONAL 24" PIPING AND MANHOLE	5	0	27OCT16A	02NOV16A
1260	UNDERSLAB PIPING AT VALVE BLDG	3	0	08DEC16A	12DEC16A
1270	FLANGE PIPE AT VALVE BLDG	3	0	13DEC16A	15DEC16A
1280	UNDERSLAB ELECTRICAL	2	0	12JAN17A	13JAN17A
1290	VALVE BLDG CONCRETE	8	0	16JAN17A	25JAN17A
1310	SET FRP BLDG	2	0	26JAN17A	27JAN17A
1320	ELECTRICAL	10	9	15FEB17A	21MAR17
1300	SET PUMPS/FLANGE DIP IN WETWELL	5	0	15FEB17A	22FEB17A
1340	CONCRETE FILL IN WETWELL	2	0	16FEB17A	17FEB17A
1350	EXPOSED SMALL PIPING	2	2	09MAR17	10MAR17
1330	PAINT WETWELL AND PIPE	5	5	23MAR17	29MAR17
HEADWORKS STRUCTURE					
1360	EXCAVATE	4	0	30AUG16A	16SEP16A
1390	UNDERSLAB DIP	1	0	06SEP16A	15SEP16A
1400	STRUCTURAL FILL	4	0	08SEP16A	16SEP16A
1440	UNDERSLAB PLUMBING	2	0	12SEP16A	16SEP16A
1370	SLAB AT 711.60	3	0	20SEP16A	23SEP16A
1410	SLAB/FOOTER @ 714.60	7	0	22SEP16A	03OCT16A
1380	WALLS FROM 711.60 TO 714.60	3	0	04OCT16A	06OCT16A
1420	WALLS	15	6	13OCT16A	16MAR17
1760	ROUGH IN ELECTRIC - 716.77 SLAB ON GRADE	2	0	14NOV16A	18NOV16A

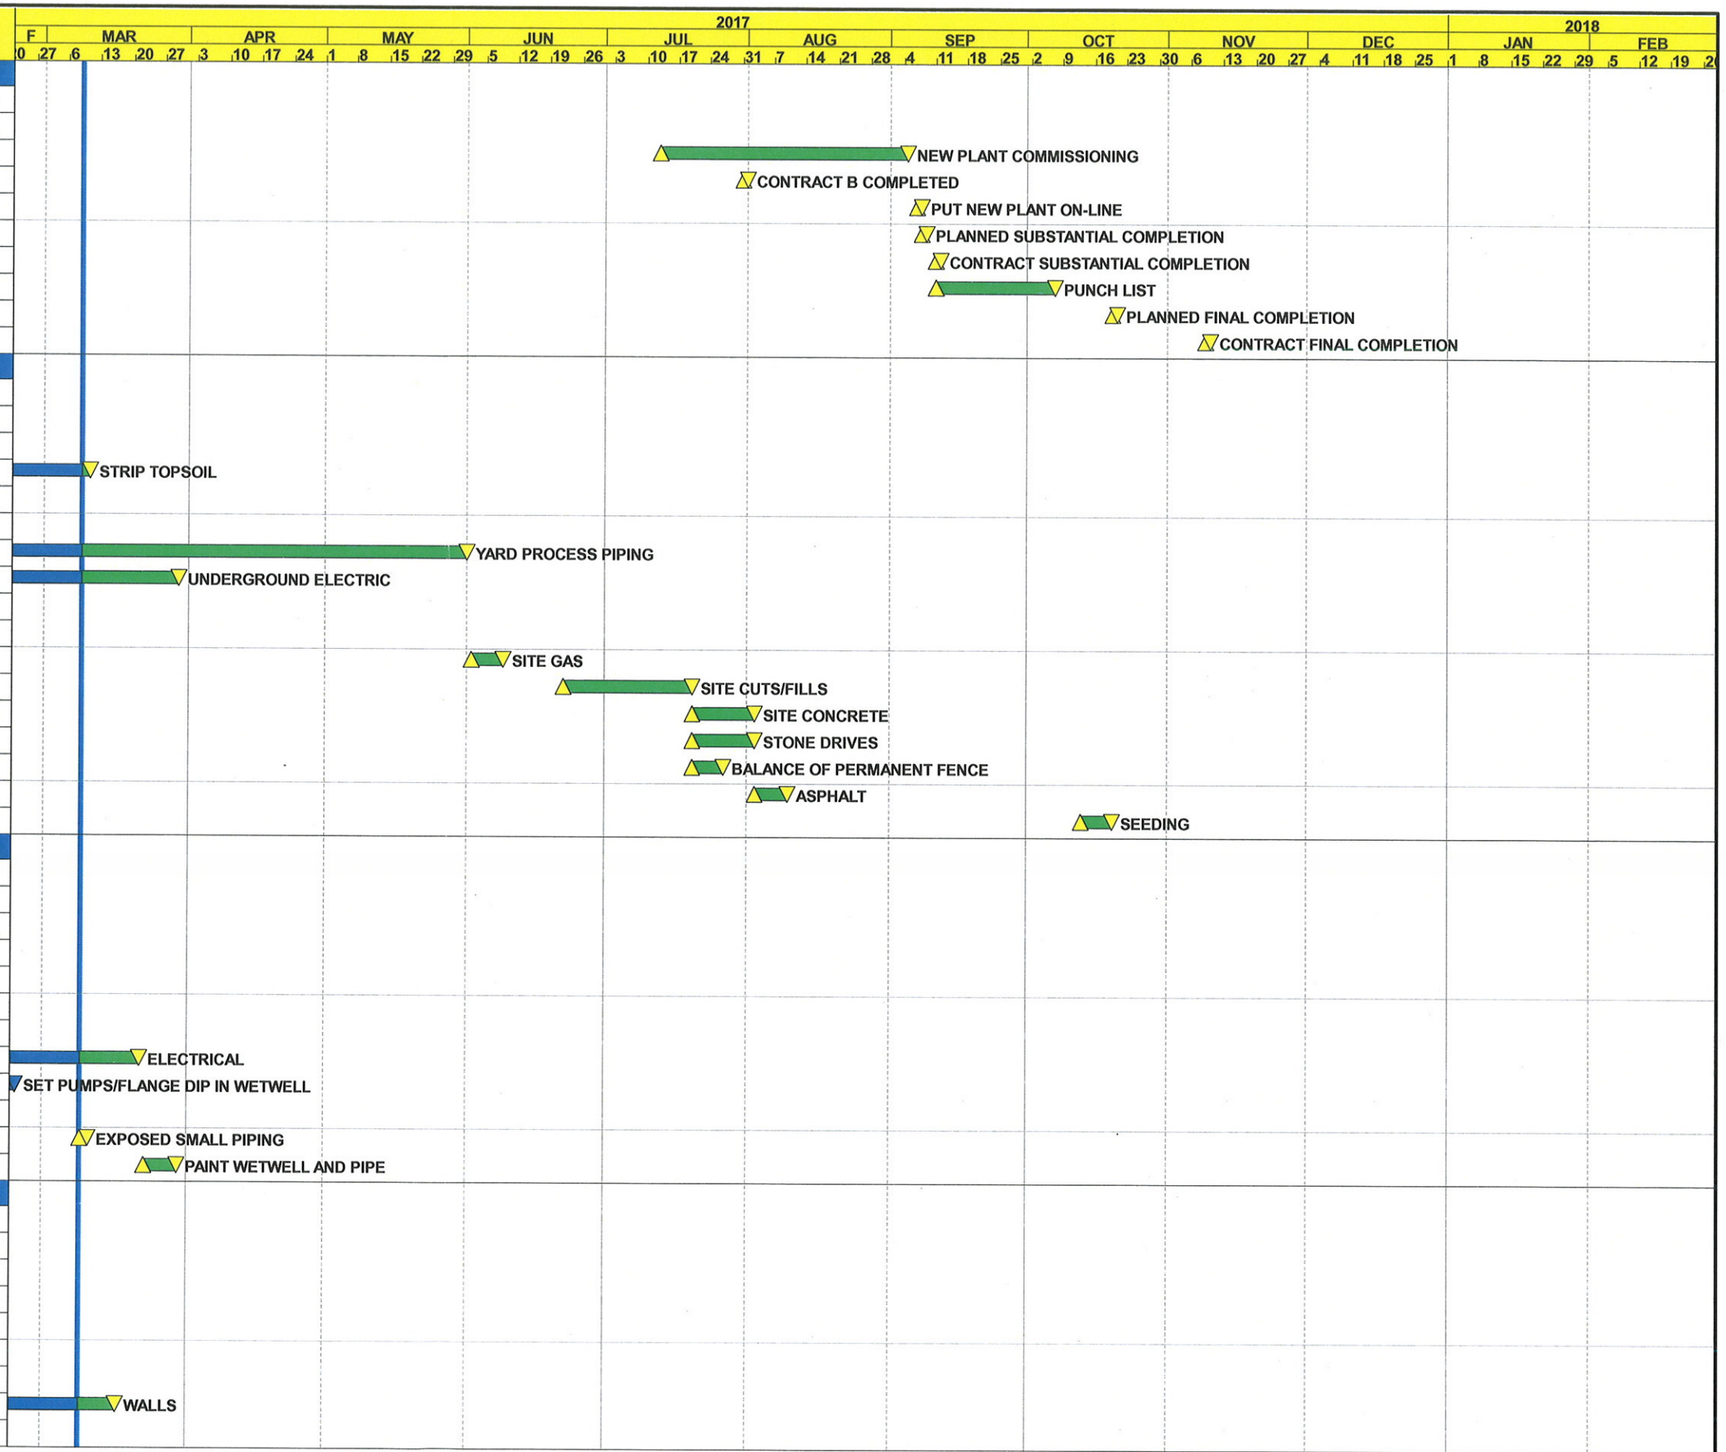

Start Date	10MAR16
Finish Date	09NOV17
Data Date	09MAR17
Run Date	08MAR17 14:40

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

ASH8

Sheet 1 of 7

PETERSON CONSTRUCTION

ASHVILLE WWTP

Classic Schedule Layout

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
1460	716.77 SLAB ON GRADE	3	0	24NOV16A	25NOV16A
1520	CMU BEARING	15	4	28NOV16A	21APR17
1670	SET MCC	1	0	06DEC16A	26DEC16A
1530	PRECAST PLANK AT ELECTRICAL ROOM	1	0	08DEC16A	08DEC16A
1680	ELECTRICAL	60	36	02JAN17A	11JUL17
1430	BACKFILL	5	5	17MAR17	23MAR17
1480	GRIT CHANNEL SLOPING SLAB	3	3	09MAR17	13MAR17
1490	GRIT CHANNEL WALLS ABOVE SLOPING SLAB	3	3	14MAR17	16MAR17
1450	PLUMBING UNDER 722.11 SLAB ON GRADE	2	2	24MAR17	27MAR17
1770	ROUGH IN ELECTRIC - 722.11 SLAB ON GRADE	2	2	24MAR17	27MAR17
1470	722.11 SLAB ON GRADE	5	5	28MAR17	03APR17
1500	GROUT FILL IN CHANNEL	5	5	04APR17	10APR17
1510	CONCRETE STAIRS	10	10	04APR17	17APR17
1560	SET SCREEN/COMPACTOR	2	2	24APR17	25APR17
1570	SET GRIT EQUIPMENT	2	2	26APR17	27APR17
1600	GATES	2	2	26APR17	27APR17
1540	PRECAST PLANK AT SCREEN ROOM	2	2	28APR17	01MAY17
1550	MASONRY PARAPETS	5	5	02MAY17	08MAY17
1580	FLANGE DIP & MUD VALVES	5	5	02MAY17	08MAY17
1660	ROOF	10	10	09MAY17	22MAY17
1620	DAMPPROOFING	3	3	09MAY17	11MAY17
1650	MASONRY VENEER	15	15	12MAY17	01JUN17
1700	HVAC	30	30	23MAY17	03JUL17
1710	PAINTING	30	30	23MAY17	03JUL17
1690	PLUMBING	25	25	23MAY17	26JUN17
1720	STOOPS, MAINTENANCE & EQUIPMENT PADS	5	5	02JUN17	08JUN17
1750	OVERHEAD DOOR	2	2	02JUN17	05JUN17
1610	METALS	10	10	09JUN17	22JUN17
1640	FRP GRATING	5	5	23JUN17	29JUN17
1590	SAMPLER & PIPING	2	2	23JUN17	26JUN17
1740	FRP DOORS	5	5	12JUL17	18JUL17
1730	DIVISION 10	1	1	19JUL17	19JUL17
1780	FLOOR SEALER	1	1	20JUL17	20JUL17
O2 SPLITTER BOX					
1790	EXCAVATION	3	3	18MAY17	22MAY17
1800	UNDERSLAB DIP	2	2	23MAY17	24MAY17
1810	BASE SLAB	5	5	25MAY17	31MAY17
1820	WALLS	10	10	01JUN17	14JUN17
1880	LEAK TEST	5	5	15JUN17	21JUN17
1830	BACKFILL	5	5	22JUN17	28JUN17
1840	GATES	3	3	29JUN17	03JUL17
1850	METALS	5	5	04JUL17	10JUL17
1860	MIXER	2	2	11JUL17	12JUL17
1870	ELECTRICAL	5	5	13JUL17	19JUL17
OXIDATION DITCH					
1890	EXCAVATION	6	0	25JUL16A	29JUL16A
1900	UNDERSLAB DIP	5	0	29JUL16A	05AUG16A
1930	MUDMAT	3	0	08AUG16A	11AUG16A
1940	BASE SLAB	15	0	15AUG16A	14SEP16A
1950	WALLS/PIERS	40	4	21SEP16A	14MAR17
2020	BACKFILL	5	0	02DEC16A	05DEC16A
2080	LEAK TEST	5	0	14DEC16A	20DEC16A

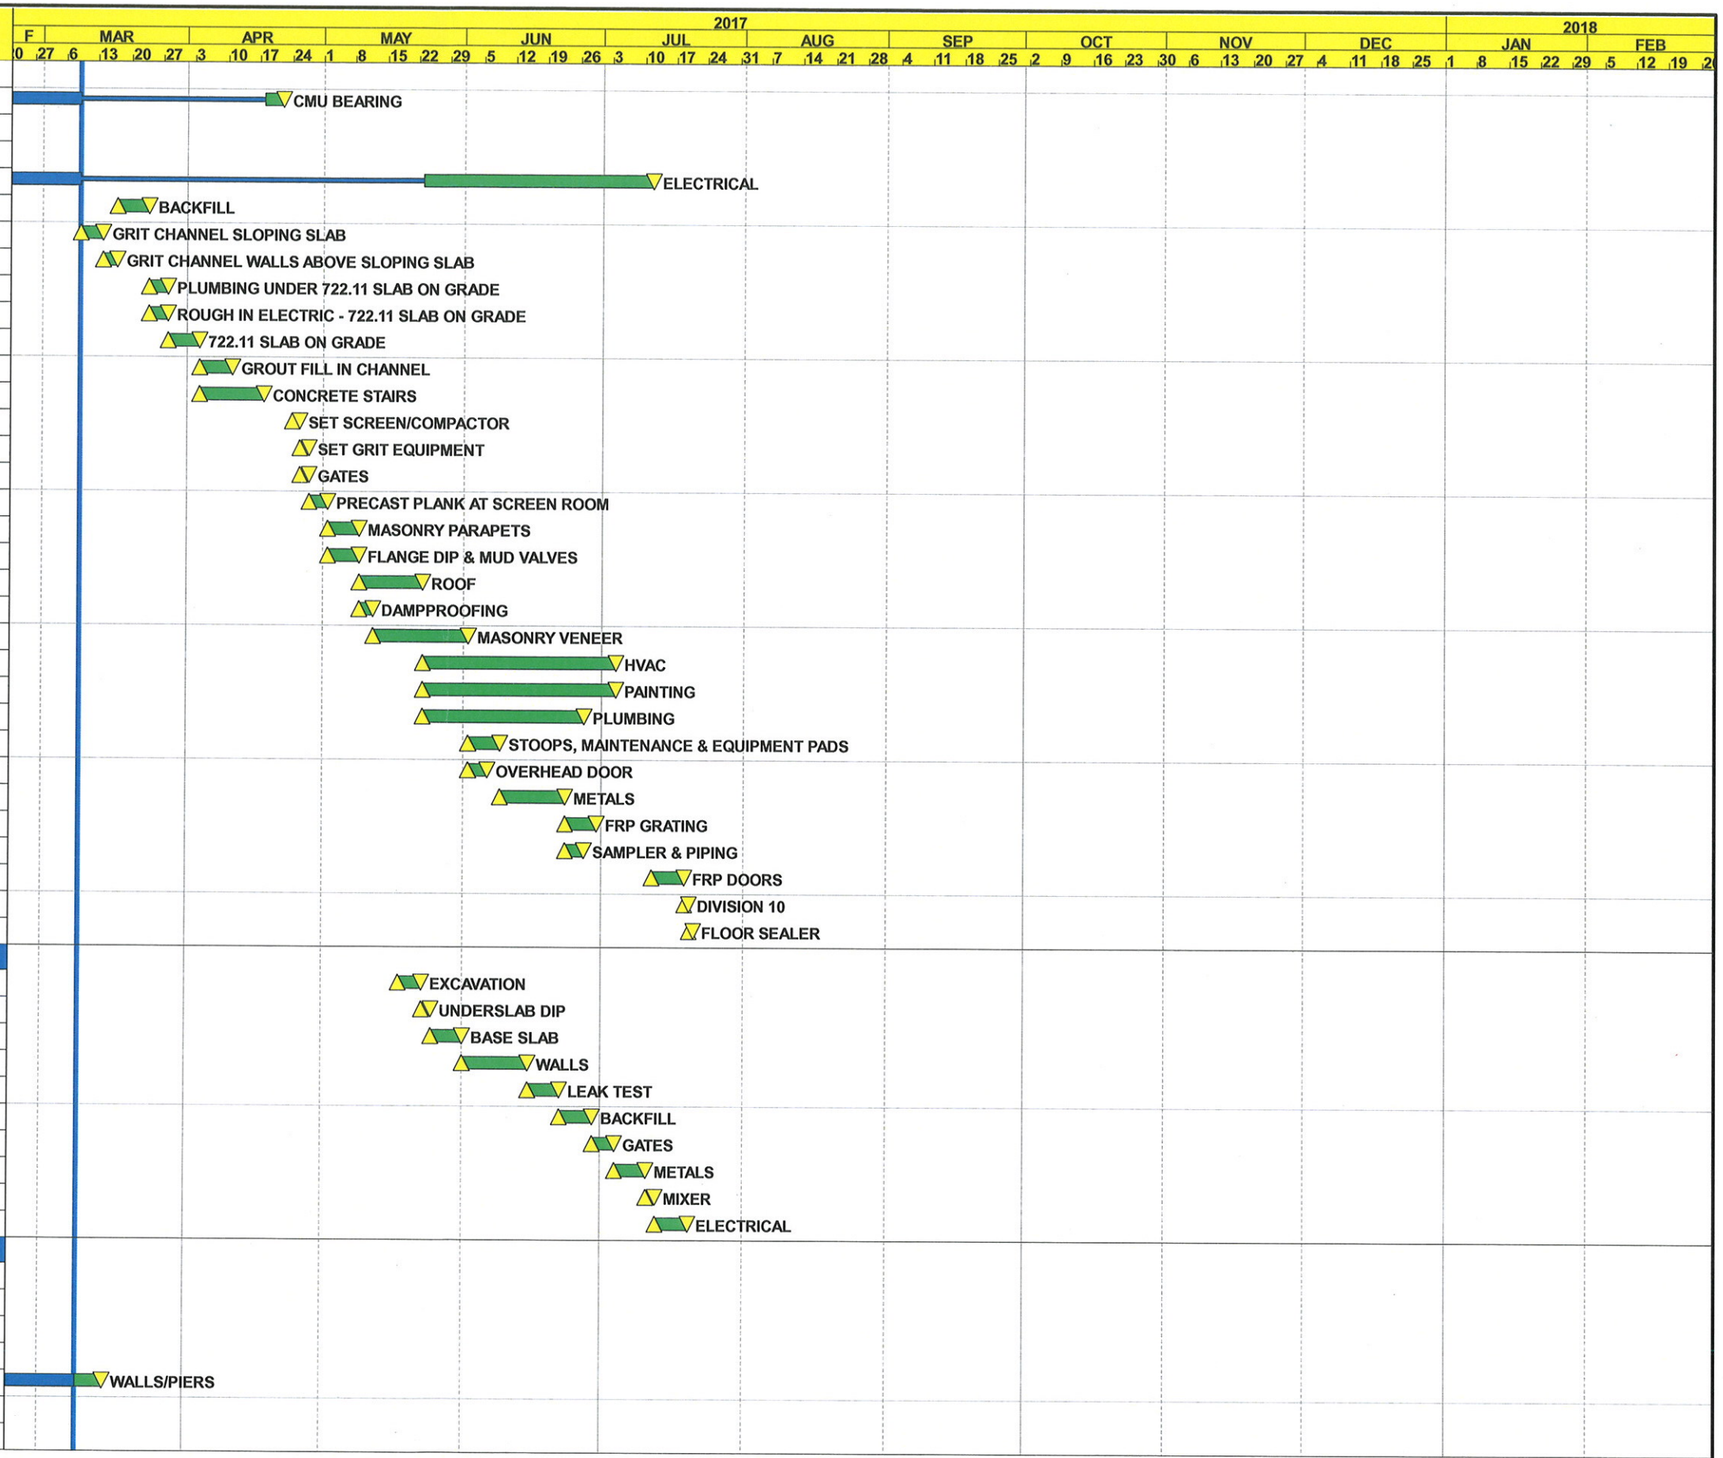

Start Date	10MAR16
Finish Date	09NOV17
Data Date	09MAR17
Run Date	08MAR17 14:40

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

ASH8

PETERSON CONSTRUCTION

ASHVILLE WWTP

Classic Schedule Layout

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
1910	SET PRECAST DRAIN VAULT	2	0	01FEB17A	02FEB17A
1920	SET PRECAST RAS VALVE VAULT	2	0	02FEB17A	02FEB17A
2040	FLANGE PIPE & VALVES	5	0	06FEB17A	07FEB17A
1980	BEARING WALKWAY DECKS	15	15	15MAR17	04APR17
1960	CENTER ISLAND FILL	3	3	15MAR17	17MAR17
2030	STAIR LANDINGS & MAINTENANCE PADS	5	5	15MAR17	21MAR17
2070	SUMP PUMPS AND PIPING	3	3	16MAR17	20MAR17
1970	CENTER ISLAND SLAB ON GRADE	4	4	20MAR17	23MAR17
2000	OXIDATION DITCH EQUIPMENT	20	20	05APR17	02MAY17
1990	METALS	15	15	03MAY17	23MAY17
2010	GATES	5	5	24MAY17	30MAY17
2060	ELECTRICAL	20	20	24MAY17	20JUN17
2050	PAINTING	5	5	24MAY17	30MAY17
CLARIFIER SPLITTER BOX					
2090	EXCAVATION	3	3	01JUN17	05JUN17
2100	UNDERSLAB DIP	2	2	06JUN17	07JUN17
2110	BASE SLAB	5	5	08JUN17	14JUN17
2120	WALLS	10	10	15JUN17	28JUN17
4020	MASONRY	2	2	29JUN17	30JUN17
2130	LEAK TEST	5	5	03JUL17	07JUL17
2140	BACKFILL	5	5	10JUL17	14JUL17
2160	GATES	3	3	17JUL17	19JUL17
2150	METALS	5	5	20JUL17	26JUL17
WEST CLARIFIER					
2170	EXCAVATION	5	0	20JUN16A	24JUN16A
2180	UNDERSLAB DIP	3	0	24JUN16A	24JUN16A
2190	MUDMAT	2	0	27JUN16A	27JUN16A
2200	BASE SLAB	10	0	27JUN16A	11JUL16A
2210	WALLS	15	0	11JUL16A	23AUG16A
2230	LEAK TEST	5	0	26SEP16A	28SEP16A
2240	BACKFILL	8	0	03OCT16A	18OCT16A
2220	LAUNDER SLAB	15	15	06APR17*	26APR17
2250	LAUNDER WALLS	10	10	13APR17	26APR17
2300	EXTERIOR BOX UNDERSLAB PIPING	2	2	27APR17	28APR17
2260	EXTERIOR BOX SLAB @ 707	3	3	01MAY17	03MAY17
2270	EXTERIOR BOX WALLS	5	5	04MAY17	10MAY17
2290	CLARIFIER MECHANISM	10	10	11MAY17*	24MAY17
2310	ELECTRICAL	10	10	25MAY17	07JUN17
2330	FRP WEIRS & SCUM BAFFLES	5	5	15JUN17	21JUN17
2280	METALS	5	5	29JUN17	05JUL17
2320	SCUM PIPING	1	1	13JUL17	13JUL17
EAST CLARIFIER					
2340	EXCAVATION	5	0	08NOV16A	11NOV16A
2350	UNDERSLAB DIP	3	0	09NOV16A	15NOV16A
2360	MUDMAT	2	0	16NOV16A	18NOV16A
2370	BASE SLAB	15	0	21NOV16A	05DEC16A
2380	WALLS	20	20	09MAR17	05APR17
2490	SCUM PIPING	1	1	09MAR17	09MAR17
2400	LEAK TEST	5	5	06APR17	12APR17
2410	BACKFILL	8	8	13APR17	24APR17
2390	LAUNDER SLAB	15	15	27APR17	17MAY17
2420	LAUNDER WALLS	10	10	04MAY17*	17MAY17

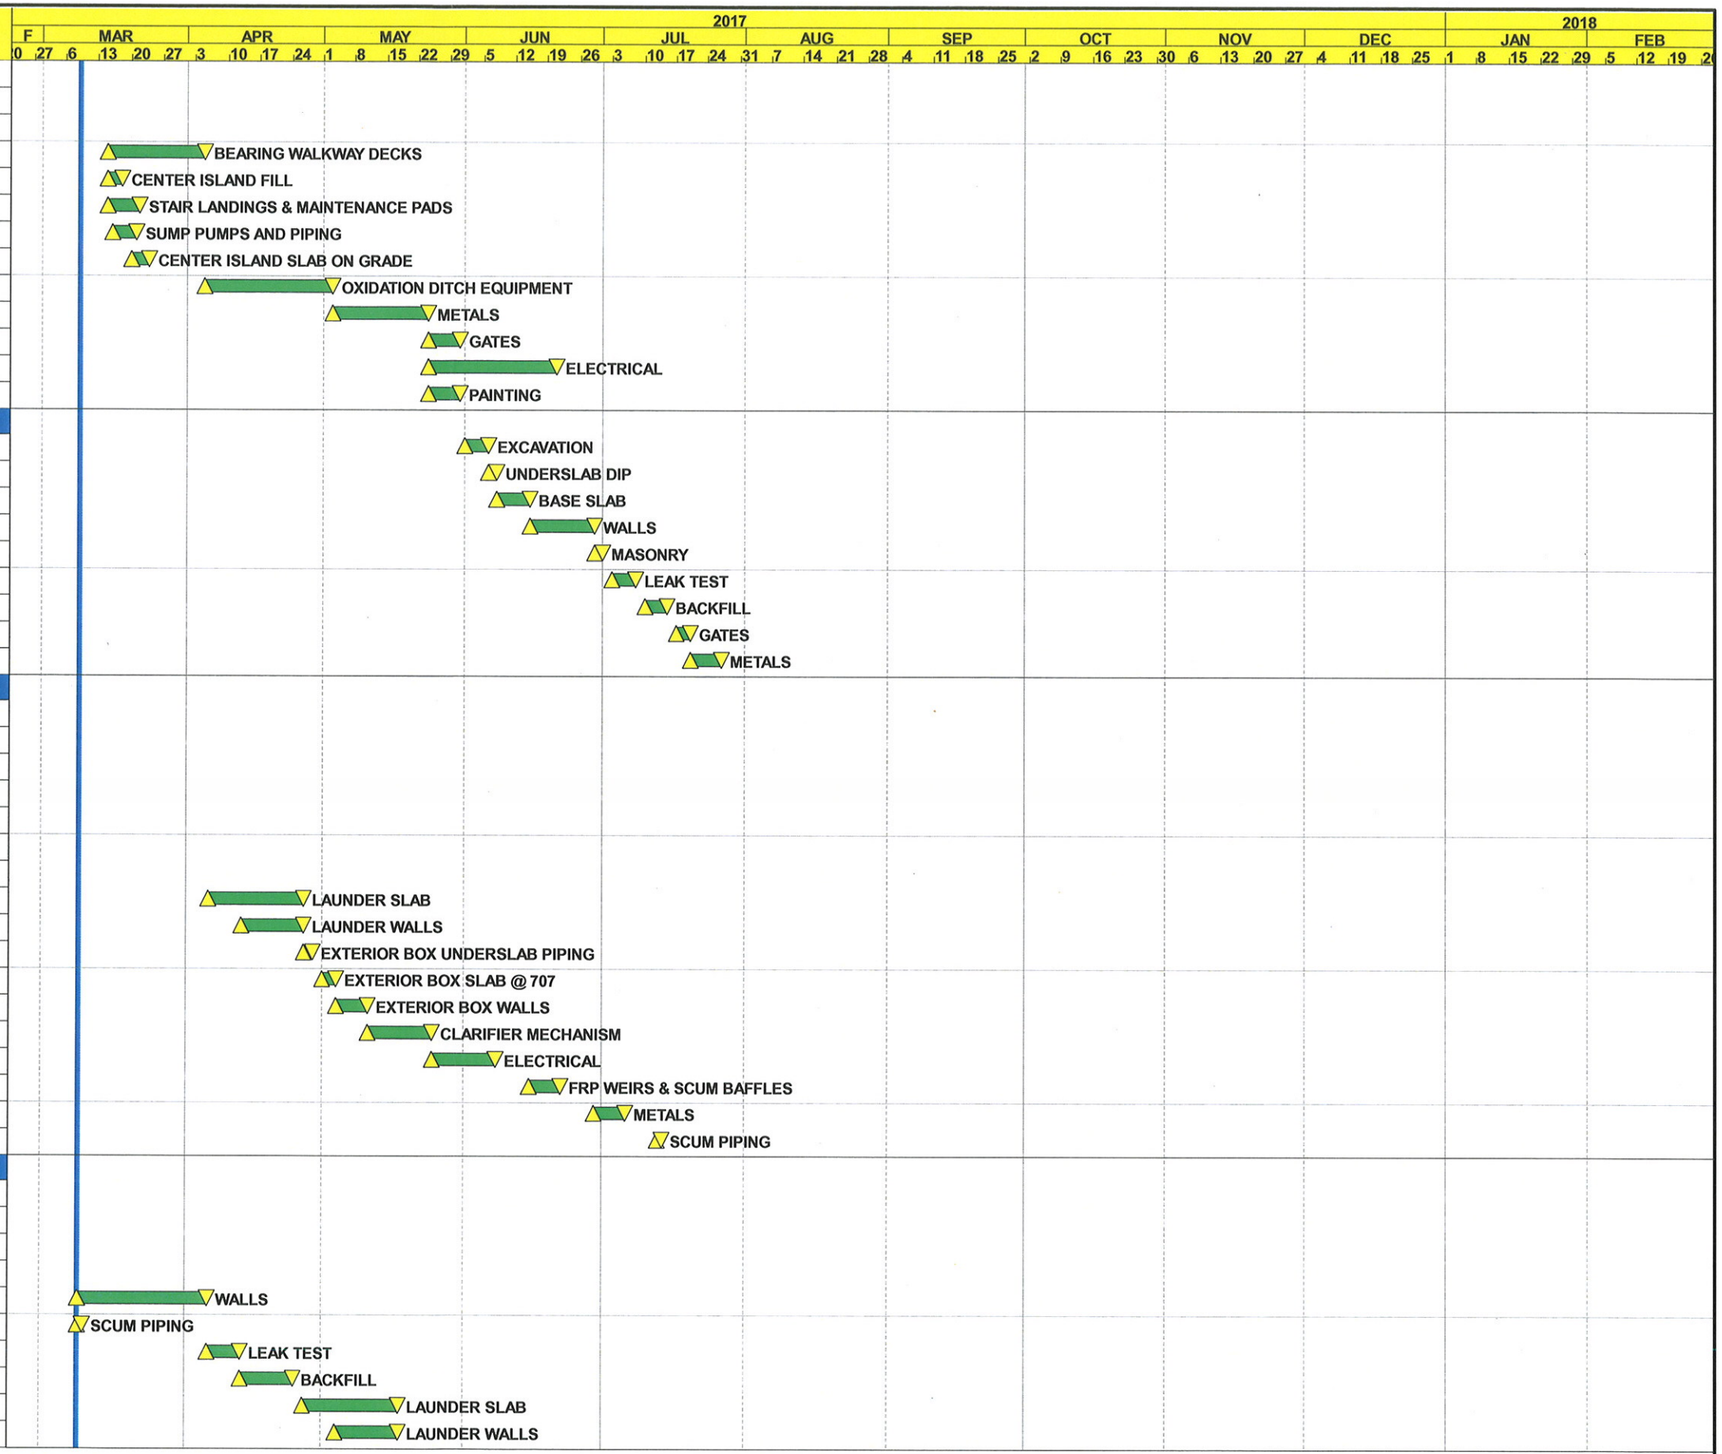

Start Date	10MAR16
Finish Date	09NOV17
Data Date	09MAR17
Run Date	08MAR17 14:40

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

ASH8

Sheet 3 of 7

PETERSON CONSTRUCTION

ASHVILLE WWTP

Classic Schedule Layout

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
2470	EXTERIOR BOX UNDERSLAB PIPING	2	2	18MAY17	19MAY17
2430	EXTERIOR BOX SLAB AT 707	3	3	22MAY17	24MAY17
2440	EXTERIOR BOX WALLS	5	5	25MAY17	31MAY17
2460	CLARIFIER MECHANISM	10	10	01JUN17	14JUN17
2480	ELECTRICAL	10	10	15JUN17	28JUN17
2500	FRP WEIRS & SCUM BAFFLES	5	5	22JUN17	28JUN17
2450	METALS	5	5	06JUL17	12JUL17
RAS/WAS PUMP STATION					
2510	EXCAVATION	5	0	06JUN16A	10JUN16A
2520	MUDMAT	1	0	13JUN16A	14JUN16A
2530	BASE SLAB	5	0	15JUN16A	17JUN16A
2540	WALLS	10	0	20JUN16A	29JUN16A
2550	LEAK TEST	5	0	12SEP16A	19SEP16A
2560	BACKFILL	5	0	01NOV16A	03NOV16A
2570	SET PRECAST VAULTS	3	0	26DEC16A	28DEC16A
2580	PUMPS & FLANGE DIP	6	6	09MAR17	16MAR17
2620	PAINT WETWELL & FLANGE DIP	5	5	17MAR17	23MAR17
2590	METALS	5	5	24MAR17	30MAR17
2610	SUMP PUMPS & PIPING	5	5	31MAR17	06APR17
2600	ELECTRICAL	5	5	07APR17	13APR17
SCUM PUMP STATION					
2630	EXCAVATE/SET WETWELL/BACKFILL	3	3	25APR17	27APR17
2640	EXCAVATE/SET VALVE VAULT/BACKFILL	2	2	28APR17	01MAY17
2650	SET PUMPS & PIPING	5	5	27JUN17	03JUL17
2670	PAINT WETWELL	2	2	04JUL17	05JUL17
2660	ELECTRICAL	5	5	06JUL17	12JUL17
UV/POST AERATION TANK					
2680	EXCAVATE	4	0	18APR16A	27APR16A
2690	MUDMAT	2	0	25APR16A	27APR16A
2700	BASE SLABS @ 695.50	5	0	28APR16A	02MAY16A
2710	WALLS - 695.50 TO 710.61	15	0	03MAY16A	27MAY16A
2800	LAUNDER SLAB	5	0	23MAY16A	25MAY16A
2720	BACKFILL BELOW 704.11 SLAB	5	0	01JUN16A	03JUN16A
2730	MUDMAT AT 704.11 SLAB	1	0	02JUN16A	02JUN16A
2750	UNDERSLAB DIP	1	0	02JUN16A	03JUN16A
2810	LAUNDER WALLS	5	0	02JUN16A	02JUN16A
2740	704.11 SLAB	5	0	06JUN16A	09JUN16A
2760	WALLS - 704.11 TO 710.61	5	0	10JUN16A	16JUN16A
2770	UV CLEANING TANK	1	0	13JUN16A	14JUN16A
2780	LEAK TEST	5	0	05JUL16A	08JUL16A
2790	BACKFILL	5	0	12JUL16A	18JUL16A
2890	GATES	5	5	15JUN17	21JUN17
2900	BLOWER PAD, MAINTENANCE PAD	5	5	15JUN17	21JUN17
2840	BLOWER, FLANGE DIP, MUD VALVES	3	3	22JUN17	26JUN17
2830	METALS	5	5	22JUN17	28JUN17
2850	AERATION SYSTEM	5	5	22JUN17	28JUN17
2860	UV EQUIPMENT	3	3	27JUN17	29JUN17
2820	FRP WEIR & TROUGHS	3	3	29JUN17	03JUL17
2870	JIB CRANE	2	2	30JUN17	03JUL17
2880	ELECTRICAL	7	7	04JUL17	12JUL17
2920	SAMPLER & PIPING	2	2	04JUL17	05JUL17
2910	SUMP PUMP & PIPING	3	3	06JUL17	10JUL17

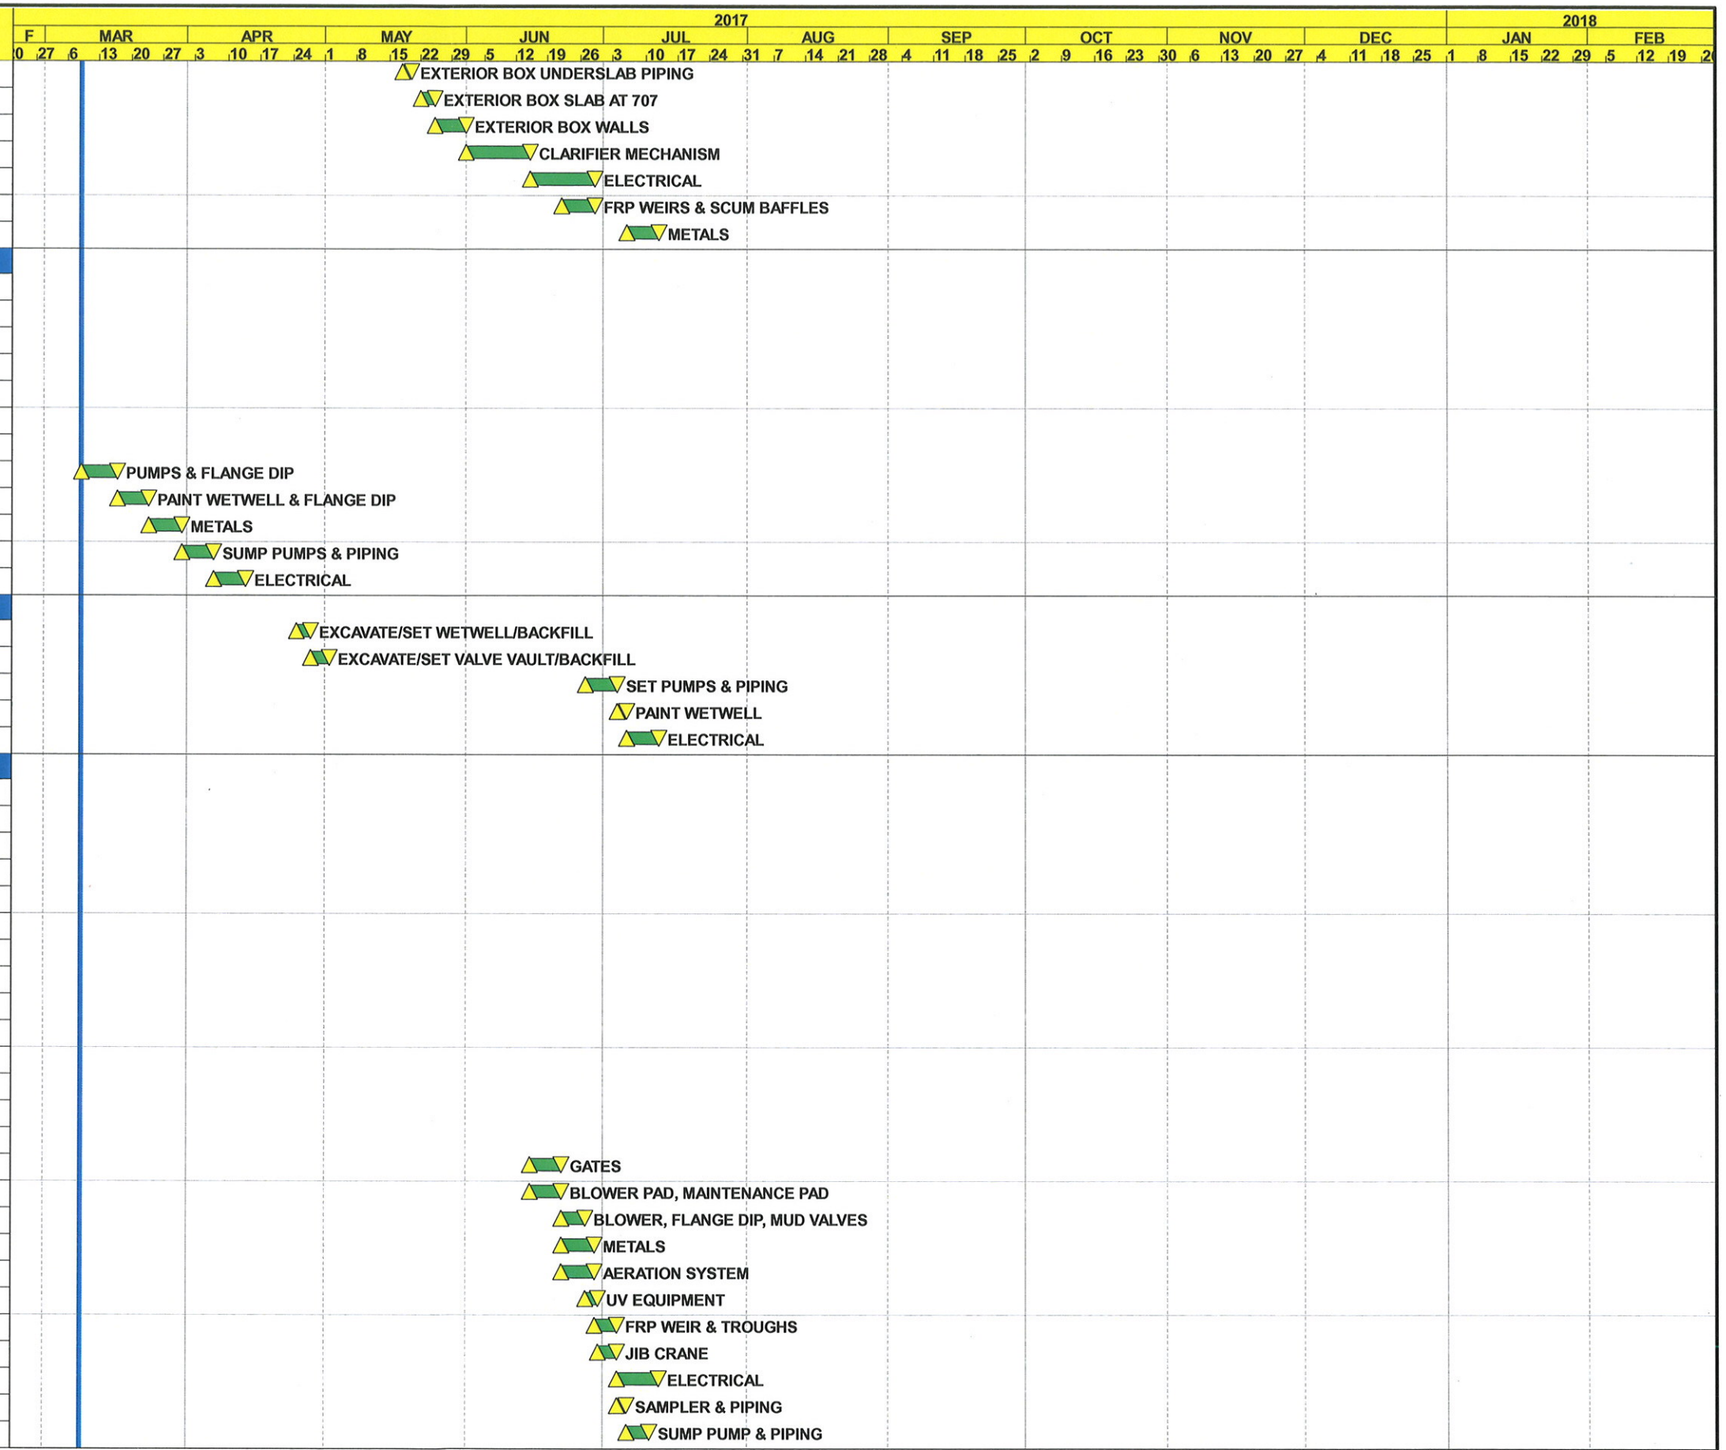

Start Date	10MAR16
Finish Date	09NOV17
Data Date	09MAR17
Run Date	08MAR17 14:40

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

ASH8

PETERSON CONSTRUCTION

ASHVILLE WWTP

Classic Schedule Layout

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
AEROBIC DIGESTERS					
2930	EXCAVATION	7	0	27APR16A	12MAY16A
2940	MUDMAT	3	0	16MAY16A	17MAY16A
2950	BASE SLAB	10	0	18MAY16A	09JUN16A
2960	WALLS	20	0	02JUN16A	18JUL16A
2970	LEAK TEST	5	0	19JUL16A	25JUL16A
2990	BACKFILL	10	0	08AUG16A	02SEP16A
3000	ADJACENT YARD DIP	5	0	11AUG16A	26AUG16A
2980	SET PRECAST VALVE VAULT	2	0	11OCT16A	11OCT16A
3030	STAIR LANDINGS	5	5	01JUN17*	07JUN17
3010	METALS	10	10	08JUN17	21JUN17
3080	GROUT FILL	5	5	08JUN17	14JUN17
3020	PUMPS & FLANGE DIP	5	5	22JUN17	28JUN17
3050	ELECTRICAL	10	10	23JUN17	06JUL17
3060	AERATION SYSTEMS	10	10	29JUN17	12JUL17
3040	PAINTING	5	5	29JUN17*	05JUL17
3070	SUMP PUMP & PIPING	3	3	29JUN17	03JUL17
SOLIDS HANDLING BLDG					
3090	UNDERSLAB DIP	3	0	26SEP16A	28SEP16A
3100	EXCAVATION/FOOTERS	5	0	28SEP16A	30SEP16A
3110	FOUNDATION WALL	7	0	10OCT16A	13OCT16A
3120	BACKFILL	2	0	13OCT16A	14OCT16A
3130	UNDERSLAB PLUMBING	3	0	17OCT16A	19OCT16A
3140	UNDERSLAB ELECTRICAL	3	0	20OCT16A	24OCT16A
3150	CUSHION FILL	2	0	20OCT16A	21OCT16A
3160	SLAB ON GRADE	5	0	25OCT16A	31OCT16A
3170	CMU BEARING	10	0	09NOV16A	22NOV16A
3200	SET PRECAST PLANK	2	0	21NOV16A	22NOV16A
3180	SET ROTARY PRESS & CONVEYORS	2	0	23NOV16A	24NOV16A
3210	MASONRY PARAPETS	5	0	23NOV16A	28NOV16A
3250	SET MCC & SWITCHGEAR	1	0	23NOV16A	23NOV16A
3290	ELECTRICAL	35	2	28NOV16A	10MAR17
3220	DAMPPROOFING	3	0	28NOV16A	28NOV16A
3300	PLUMBING	20	16	01DEC16A	30MAR17
3230	ROOF	10	0	05DEC16A	07DEC16A
3240	MASONRY VENEER	10	0	05DEC16A	19DEC16A
3380	METALS	2	1	06DEC16A	13MAR17
3280	PAINTING	20	3	06FEB17A	13MAR17
3350	SCH. 80 PVC PROCESS DRAIN/VENT PIPING	2	0	07FEB17A	07FEB17A
3260	FRP GRATING	1	0	01MAR17A	02MAR17A
3370	OVERHEAD DOOR	2	0	01MAR17A	02MAR17A
3310	HVAC	25	25	09MAR17	12APR17
3320	STOOPS & BLOWER CONCRETE	10	10	09MAR17	22MAR17
3340	FLANGE PIPE IN BUILDING	2	2	09MAR17	10MAR17
3360	FRP DOORS	3	3	13MAR17	15MAR17
3190	POLYMER SYSTEM & PIPING	3	3	14MAR17	16MAR17
3270	DIVISION 10	1	1	16MAR17	16MAR17
3390	FLOOR SEALER	1	1	17MAR17	17MAR17
3330	SET BLOWERS & FLANGE DIP	5	5	27JUN17	03JUL17
SLUDGE CAKE PAD					
3400	EXCAVATION/FOOTERS	5	5	29JUN17*	05JUL17
3410	WALLS/PIERS	10	10	06JUL17	19JUL17

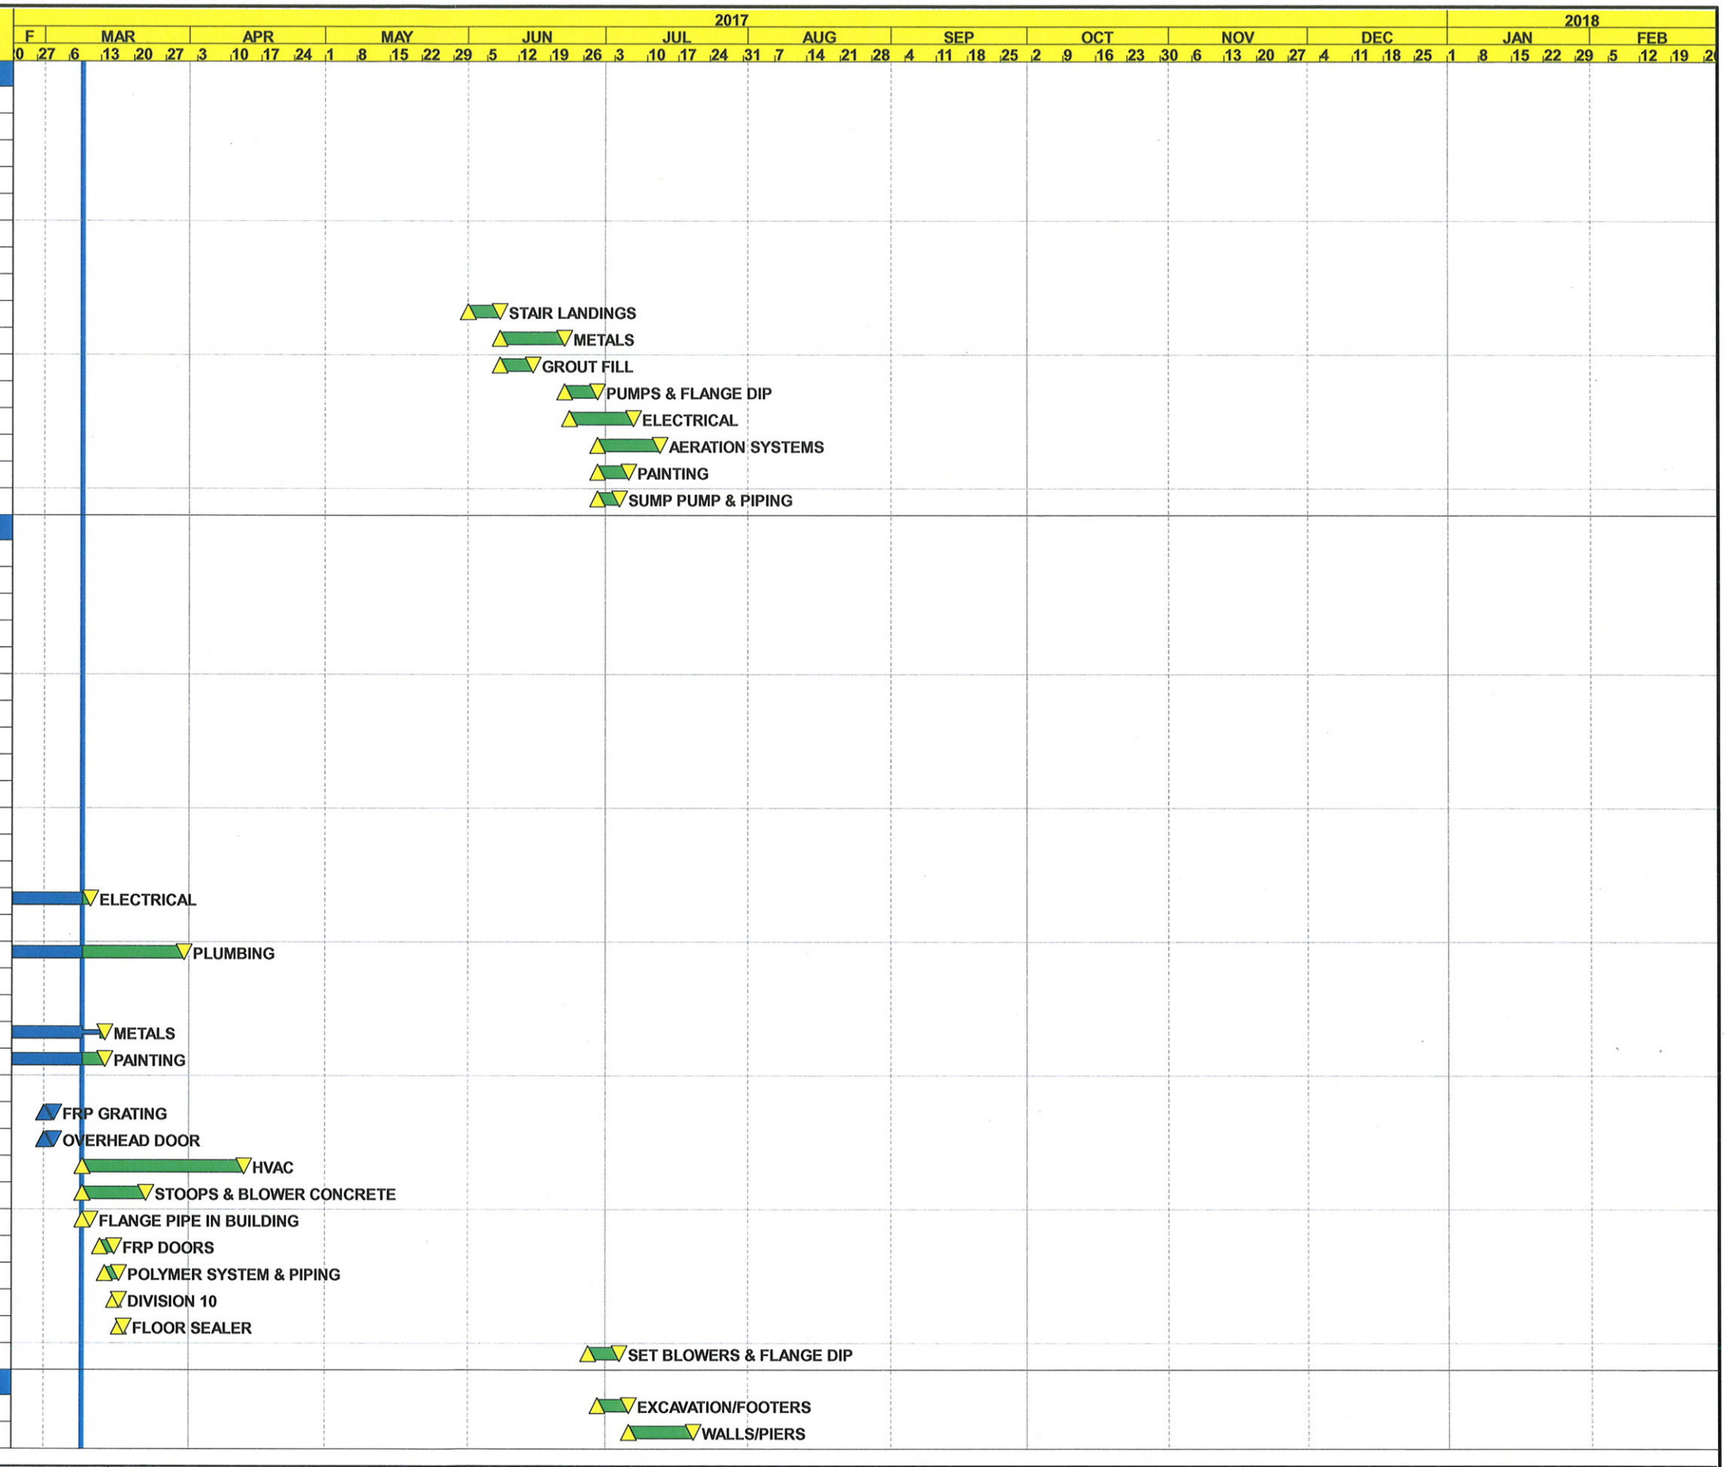

Start Date	10MAR16
Finish Date	09NOV17
Data Date	09MAR17
Run Date	08MAR17 14:40

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

ASH8

Sheet 5 of 7

PETERSON CONSTRUCTION

ASHVILLE WWTP

Classic Schedule Layout

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
3420	BACKFILL	3	3	20JUL17	24JUL17
3450	UNDERSLAB PLUMBING/TRENCH DRAIN	3	3	25JUL17	27JUL17
3430	SLAB ON GRADE	7	7	28JUL17	07AUG17
3440	PRE-ENGINEERED METAL BUILDING	15	15	08AUG17	28AUG17
ADMINISTRATION BLDG					
3460	EXCAVATION/FOOTERS	5	5	11APR17	17APR17
3470	FOUNDATION WALL	5	5	18APR17	24APR17
3480	BACKFILL	2	2	25APR17	26APR17
3490	UNDERSLAB PLUMBING	3	3	27APR17	01MAY17
3500	CUSHION FILL	3	3	02MAY17	04MAY17
3510	UNDERSLAB ELECTRICAL	2	2	05MAY17	08MAY17
3520	SLAB ON GRADE	5	5	18MAY17	24MAY17
3560	STOOPS & EQUIPMENT PADS	5	5	25MAY17	31MAY17
3530	PRE-ENGINEERED WOOD FRAME BLDG	20	20	01JUN17	28JUN17
3540	EXTERIOR MANDOORS	3	3	29JUN17	03JUL17
3550	OVERHEAD DOOR	2	2	29JUN17	30JUN17
3570	GYPSUM BOARD CEILING	3	3	04JUL17	06JUL17
3590	METAL STUDS	5	5	07JUL17	13JUL17
3580	ATTIC BLOWN INSULATION	2	2	07JUL17	10JUL17
3610	WALL ROUGH INS	10	10	14JUL17	27JUL17
3600	ABOVE CEILING PME ROUGH INS	15	15	14JUL17	03AUG17
3620	GYPSUM BOARD ON WALLS	5	5	28JUL17	03AUG17
3770	ELECTRICAL FINISHES	20	20	04AUG17	31AUG17
3630	ACOUSTICAL CEILING GRID	3	3	04AUG17	08AUG17
3740	PAINTING	15	15	04AUG17	24AUG17
3750	PLUMBING FINISHES	15	15	04AUG17	24AUG17
3760	HVAC FINISHES	15	15	04AUG17	24AUG17
3690	EPOXY FLOORING	5	5	09AUG17	15AUG17
3640	ABOVE CEILING INSPECTION	1	1	09AUG17	09AUG17
3710	CERAMIC TILE	3	3	09AUG17	11AUG17
3670	LIGHTS/DIFFUSERS	3	3	10AUG17	14AUG17
3660	LAB CASEWORK	3	3	16AUG17	18AUG17
3700	INTERIOR DOORS	3	3	16AUG17	18AUG17
3680	BREAKROOM CASEWORK	2	2	21AUG17	22AUG17
3720	VCT	3	3	23AUG17	25AUG17
3650	DROP PADS	2	2	28AUG17	29AUG17
3730	DIVISION 10	2	2	30AUG17	31AUG17
3780	FLOOR SEALER	1	1	01SEP17	01SEP17
SITEWORK - EXISTING WWTP					
3860	INSTALL NEW MDP PANEL & HEAT UP	10	10	29JUN17	12JUL17
3850	UNDERGROUND ELECTRIC TO NEW PUMP	5	5	13JUL17	19JUL17
3890	START UP PUMP STATION	2	2	17AUG17	18AUG17
3790	TIE-IN SANITARY TO PUMP STATION	2	2	05SEP17	06SEP17
3840	PUMP TANK CONTENTS TO PUMP STATION	3	3	05SEP17	07SEP17
3800	BULK DEMO	15	15	15SEP17	05OCT17
3830	SELECTIVE DEMO IN EXISTING STRUCTURES	5	5	15SEP17	21SEP17
3870	ELECTRICAL DEMO	10	10	15SEP17	28SEP17
3820	GRINDER PUMP STATION & DISCHARGE PIPING	5	5	22SEP17	28SEP17
3880	ELECTRICAL TO GRINDER PUMP STATION	5	5	29SEP17	05OCT17
3810	SEEDING	5	5	06OCT17	12OCT17
3900	START UP GRINDER PUMP STATION	1	1	06OCT17	06OCT17

Start Date	10MAR16
Finish Date	09NOV17
Data Date	09MAR17
Run Date	08MAR17 14:40

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

ASH8

Sheet 6 of 7

PETERSON CONSTRUCTION

ASHVILLE WWTP

Classic Schedule Layout

Date	Revision	Checked	Approved

Activity ID	Activity Description	Orig Dur	Rem Dur	Early Start	Early Finish
PUMP STATION - EXISTING WWTP					
3910	EXCAVATE/SET WETWELL/BACKFILL	5	5	29JUN17	05JUL17
3920	UNDERSLAB PIPING	3	3	06JUL17	10JUL17
3930	FLANGE PIPE AT VALVE BLDG	3	3	11JUL17	13JUL17
4010	UNDERSLAB ELECTRICAL	2	2	14JUL17	17JUL17
3940	VALVE BLDG CONCRETE	7	7	18JUL17	26JUL17
3950	WETWELL PUMPS & FLANGE DIP	4	4	27JUL17	01AUG17
3970	SET FRP BLDG	2	2	02AUG17	03AUG17
3960	PAINT WETWELL & FLANGE DIP	5	5	02AUG17	08AUG17
3990	EXPOSED SMALL PIPING	2	2	04AUG17	07AUG17
3980	ELECTRICAL	7	7	08AUG17	16AUG17

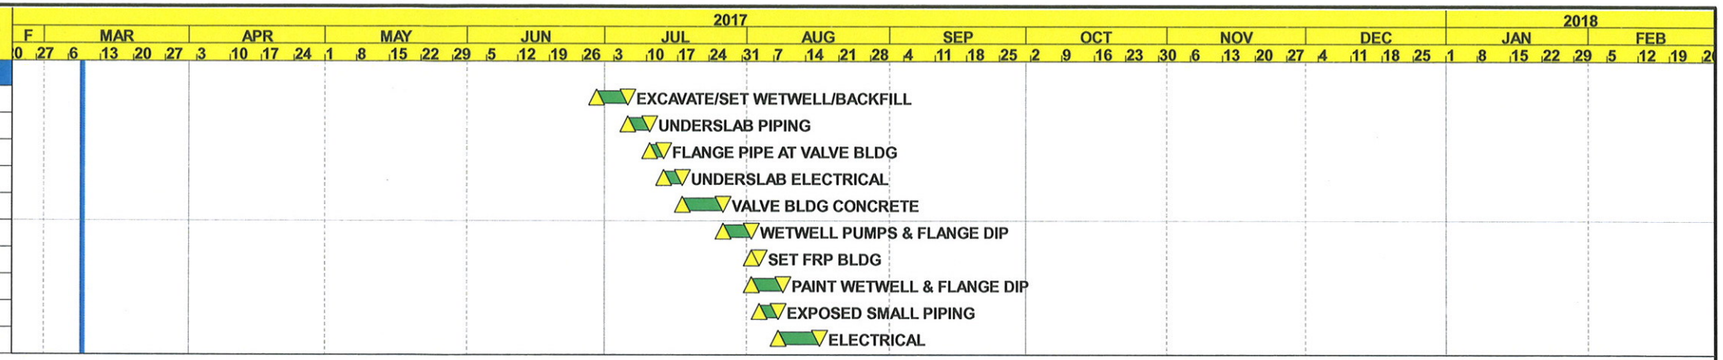

Start Date	10MAR16
Finish Date	09NOV17
Data Date	09MAR17
Run Date	08MAR17 14:40

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

ASH8

Sheet 7 of 7

PETERSON CONSTRUCTION

ASHVILLE WWTP

Classic Schedule Layout

Date	Revision	Checked	Approved
